

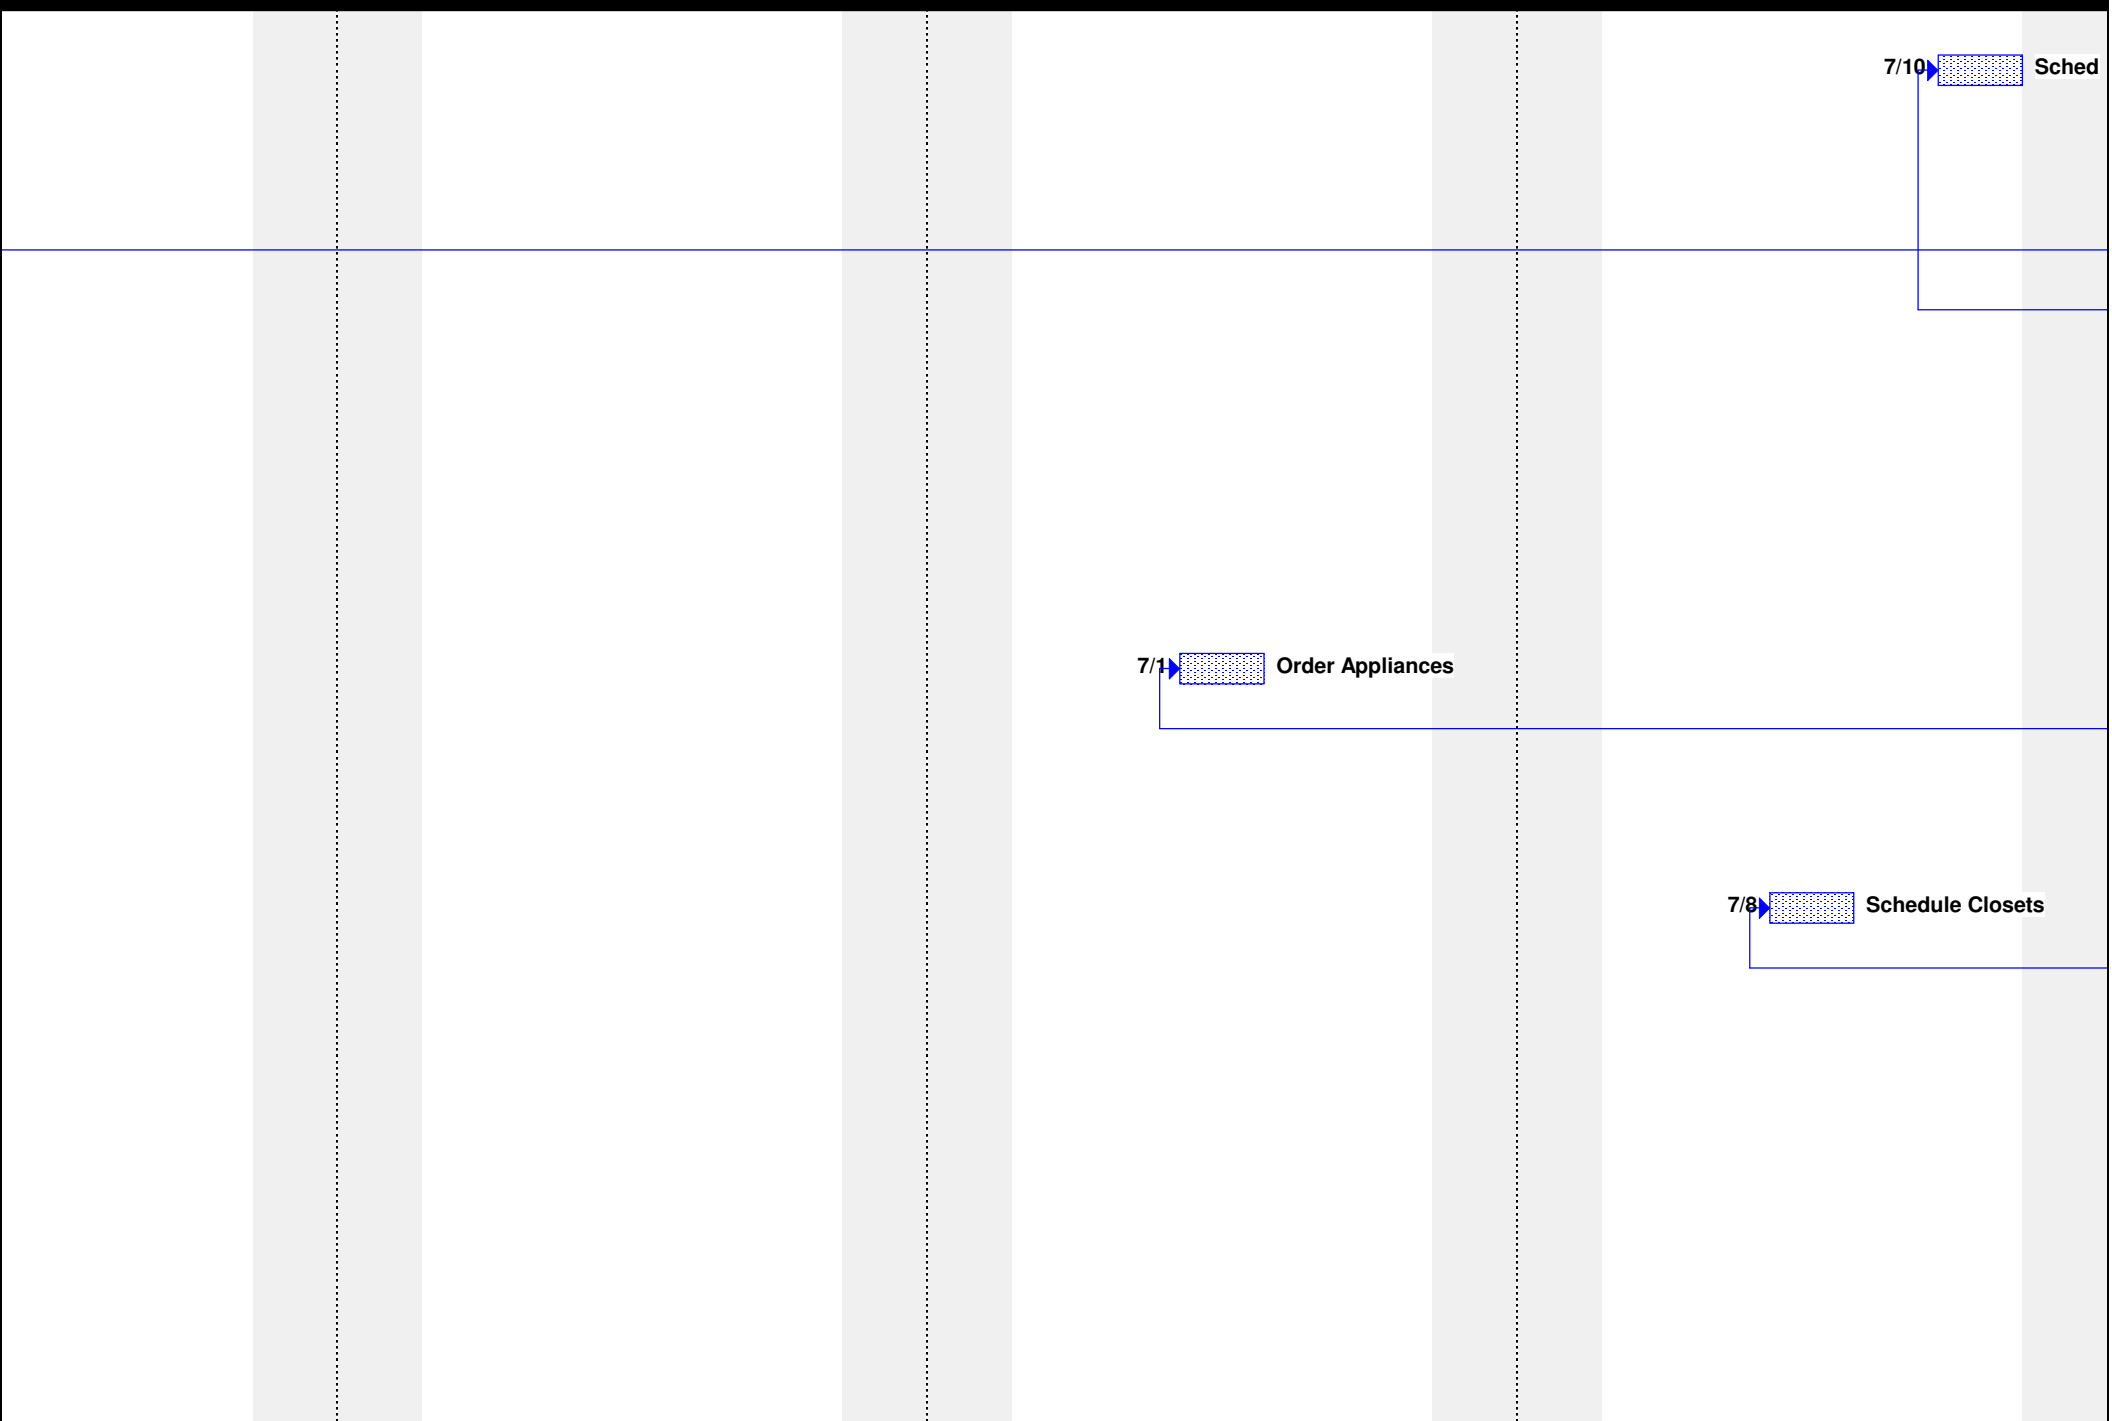


ID	Task Name	Duration	as of	Start	Finish	Pr	Resource Names	9							Jun 14, '09		
								M	T	W	T	F	S	S	M	T	
1	Total Project	116 days		Mon 3/9/09	Mon 8/17/09												
2	Further Work	116 days		Mon 3/9/09	Mon 8/17/09												
3	Rockwork	5 days	4	Tue 6/23/09	Mon 6/29/09		KHB Rock Crew										
4	Install Gutters	2 days	0	Thu 7/2/09	Fri 7/3/09	3,7	Gutter Vendor										
5	Install Decking	6 days	2	Mon 6/15/09	Mon 6/22/09		KHB Siding								6/15		
6	Exterior Handrails	4 days	2	Tue 6/23/09	Fri 6/26/09	5	KHB Siding										
7	Paint Exterior	10 days	0	Thu 6/18/09	Wed 7/1/09	5F	Painting Vendor										
8	Mechanical	27 days		Mon 3/9/09	Tue 4/14/09												
19	Paint Garage Door	2 days		Mon 6/29/09	Tue 6/30/09	7F	Painting Vendor										
20	Install Garage Door	1 day		Wed 7/1/09	Wed 7/1/09	19	Garage Door Vendor										
21	Measure / Order Cabinets	1 day		Tue 6/16/09	Tue 6/16/09		Cabinet Vendor[50%],									6/16	
22	Durrock Install	2 days		Mon 6/15/09	Tue 6/16/09		Tile Vendor								6/15		
23	Prime Drywall	2 days		Mon 6/15/09	Tue 6/16/09		Painting Vendor								6/15		
24	Drywall Touch-up	1 day		Tue 6/16/09	Tue 6/16/09	23	Drywall Vendor								6/16		
25	1st Coat interior Paint	4 days		Wed 6/17/09	Mon 6/22/09	24	Painting Vendor										6/17
26	Order Hardwood	1 day		Fri 6/12/09	Fri 6/12/09	27	KHB Production							6/12		Order Hardwood	
27	Hardwood Deliver	1 day		Fri 6/26/09	Fri 6/26/09	29	Hardwood Vendor										
28	Draw Schedule - Hardwood	1 day		Mon 6/29/09	Mon 6/29/09	27											
29	Hardwood Install	6 days		Wed 7/8/09	Wed 7/15/09	34	Hardwood Vendor										
30	Shower Pans	1 day		Wed 6/17/09	Wed 6/17/09	22	Tile Vendor										6/17
31	Shower Pan inspection	1 day		Thu 6/18/09	Thu 6/18/09	30	Building Department										
32	Install Tile	8 days		Fri 6/19/09	Tue 6/30/09	31	Tile Vendor										
33	Order Interior Doors	1 day		Tue 6/9/09	Tue 6/9/09	34	KHB Production							6/9		Order Interior Doors	
34	Interior Trim / Panel	11 days		Tue 6/23/09	Tue 7/7/09	25	KHB Trim										
35	Install Cabinet/Vanity	2 days		Thu 7/16/09	Fri 7/17/09	29	Cabinet Vendor										
36	Measure Tops	1 day		Mon 7/20/09	Mon 7/20/09	35	Counter Top Vendor										
37	Mechanical Trim	38 days		Fri 6/12/09	Tue 8/4/09												
38	Schedule Mechanical Trim-out	1 day		Fri 7/10/09	Fri 7/10/09	42	KHB Production										
39	Plumbing Trim	5 days		Mon 7/27/09	Fri 7/31/09	47	Plumbing Vendor										
40	Order Light Fixtures	1 day		Fri 6/12/09	Fri 6/12/09	41	KHB Production							6/12		Order Light Fixtures	
41	Light Fixture Delivery	1 day		Fri 7/24/09	Fri 7/24/09	42	Electrical Vendor										
42	Electric Trim	6 days		Fri 7/24/09	Fri 7/31/09	50	Electrical Vendor										
43	HVAC Trim	4 days		Tue 7/28/09	Fri 7/31/09	50	HVAC Vendor										
44	Security Trim	2 days		Mon 8/3/09	Tue 8/4/09	42	Security Vendor										
45	Audio Trim	2 days		Mon 8/3/09	Tue 8/4/09	42	Audio Vendor										
46	Lightning Rod Trim	1 day		Mon 8/3/09	Mon 8/3/09	42	Lightning Rod Vendor										
47	Install Counter Tops	2 days		Tue 7/28/09	Wed 7/29/09	36	Counter Top Vendor										
48	Order Appliances	1 day		Wed 7/1/09	Wed 7/1/09	49	KHB Production										
49	Appliance Deliver	1 day		Wed 7/29/09	Wed 7/29/09	50	Appliance Vendor										
50	Appliance Install	1 day		Thu 7/30/09	Thu 7/30/09	39	Appliance Vendor										
51	Misc. Punch	5 days		Mon 8/3/09	Fri 8/7/09	37	KHB Trim										
52	Schedule Closets	1 day		Wed 7/8/09	Wed 7/8/09	53	KHB Production										
53	Closet Install	1 day		Wed 8/5/09	Wed 8/5/09	37	Closet Vendor										
54	Schedule/Order Carpet	1 day		Thu 7/16/09	Thu 7/16/09	55	KHB Production										
55	Carpet	2 days		Thu 8/6/09	Fri 8/7/09	53	Carpet Vendor										
56	Final Inspections	1 day		Wed 8/5/09	Wed 8/5/09	37	Building Department										
57	Draw Schedule - CO	1 day		Thu 8/6/09	Thu 8/6/09	56											
58	Paint Touch-up	2 days		Mon 8/10/09	Tue 8/11/09	55	Painting Vendor										
59	Final Clean	3 days		Wed 8/12/09	Fri 8/14/09	51	Cleaning Vendor										
60	Draw Schedule - Final	1 day		Mon 8/17/09	Mon 8/17/09	59											

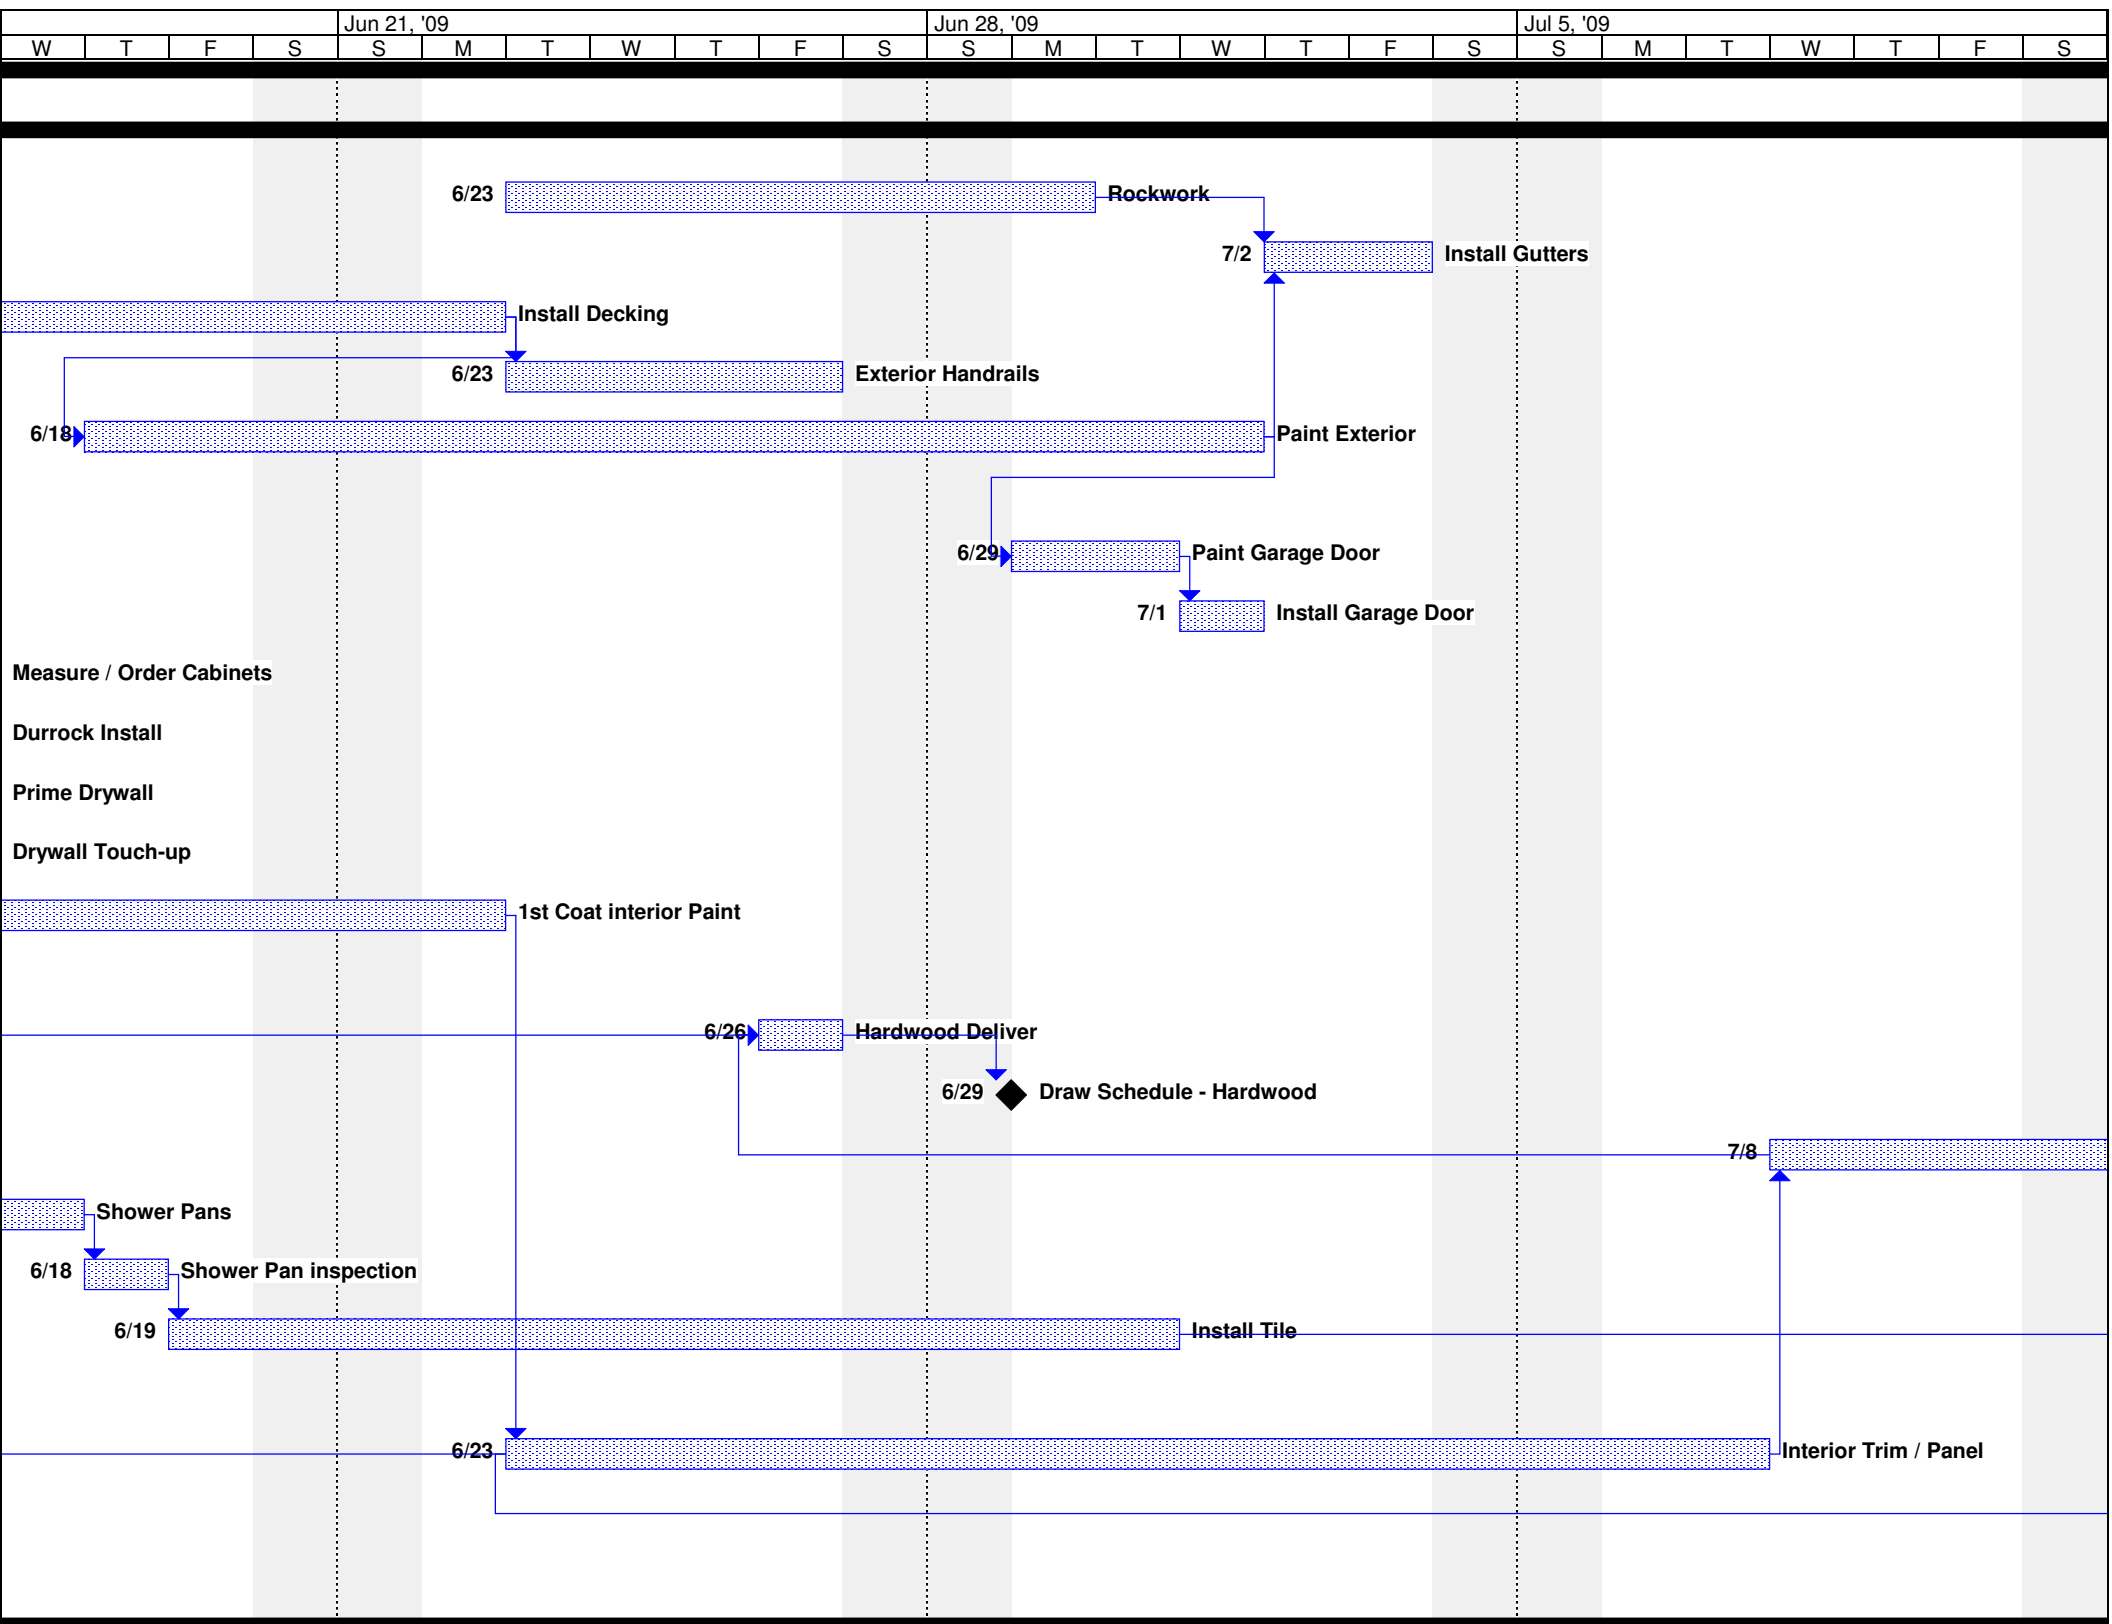

Jul 12, '09							Jul 19, '09							Jul 26, '09							Aug 2, '09			
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W

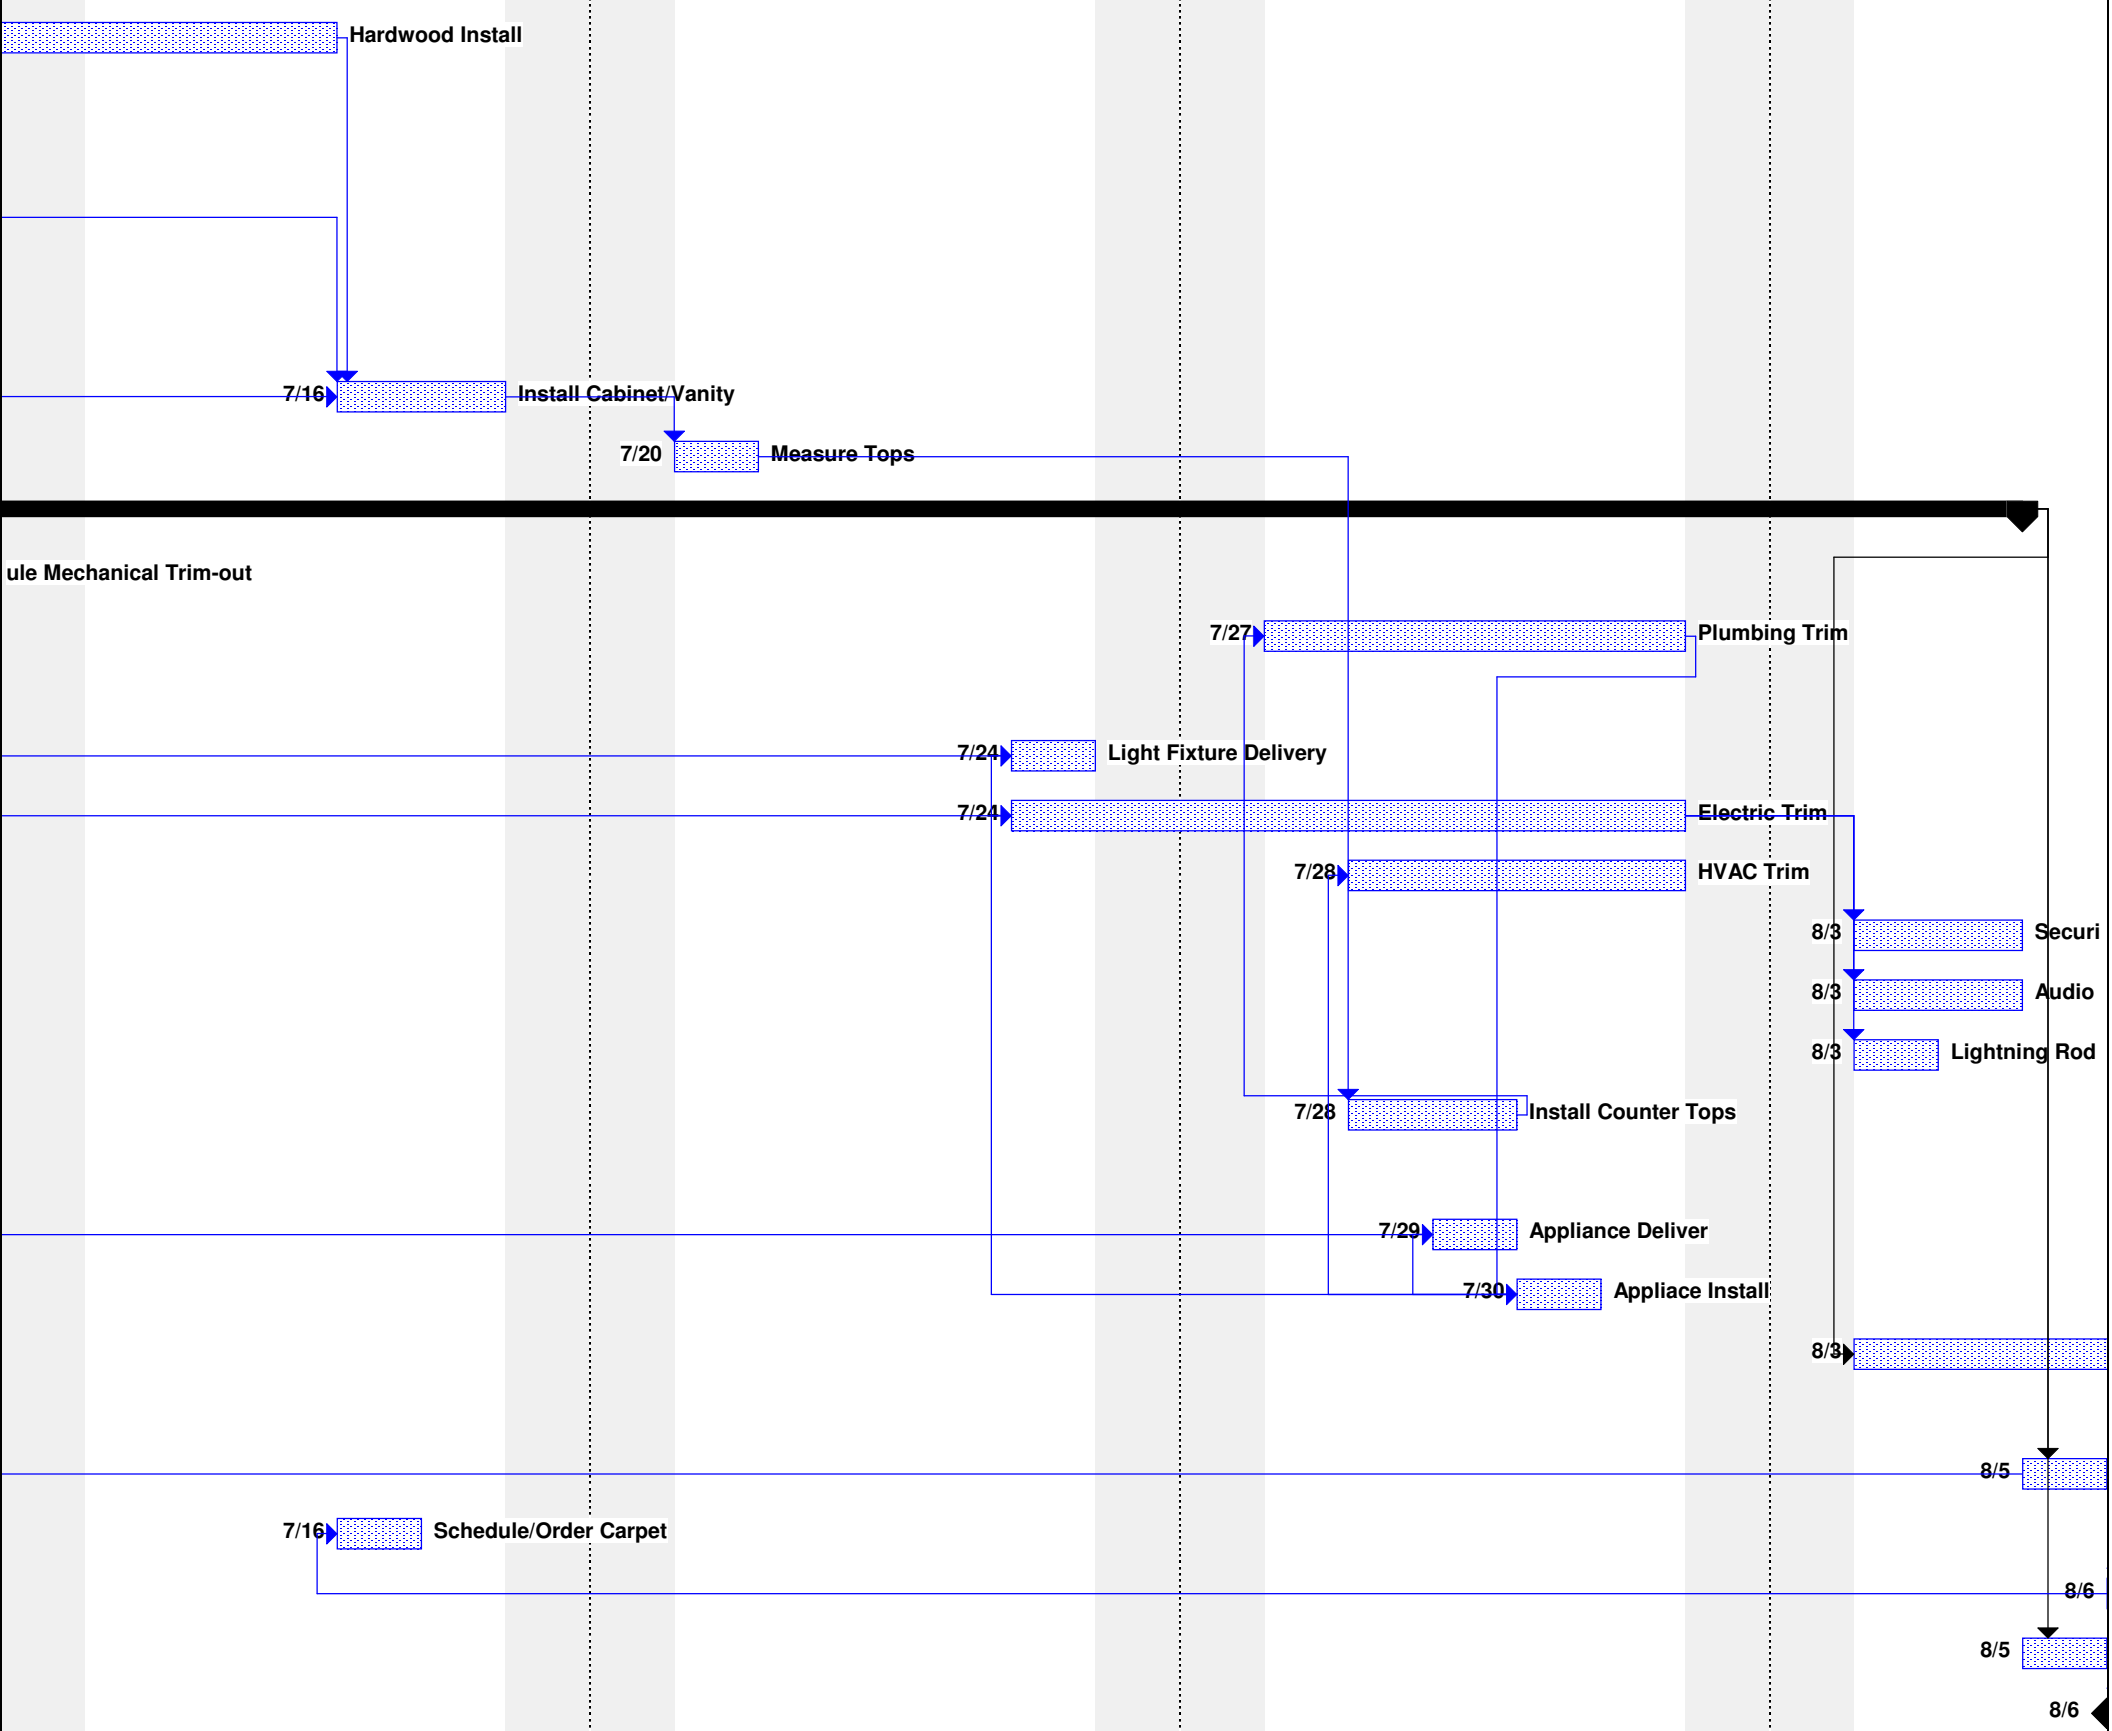

Aug 9, '09							Aug 16, '09							Aug 23, '09							Aug 30, '09			
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

ity Trim
Trim
Trim

